




# THE REHABILITATION AND RECONSTRUCTION LOAN (RRL)

## MONTHLY PROGRESS REPORT

FEBRUARY 2019 ISSUE

### CONSULTANCIES

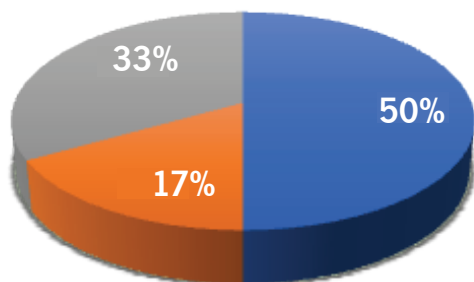

■ Signed  
■ Contract Awarded  
■ Tender phase

**TOTAL BUDGET OF 18 CONSULTANCIES  
\$8,102,000 USD**

- 9 of 18 consultancies have been signed
- 3 consultancies have been awarded contracts (to be signed)
- 6 consultancies are in tender phase

#### CONTRACTS SIGNED:

1. Security (Police ICT)
2. DDM Building
3. Other Government Buildings
4. DDM Equipment
5. Psycho Social PAHO
6. IST (Implementation Support Team)

- FEB. UPDATE
7. Water consultant
  8. Project Engineer
  9. Roads, Slopes and Coastal Defences

**UPDATED TOTAL: \$3,965,877 USD**

#### CONTRACTS AWARDED (to be signed):

10. Financial Audit Services
- FEB. UPDATE
11. Construction Management of Bregado Flax
  12. Climate Risk Vulnerability Assessment (CVA)


**UPDATED Total: \$313,658 USD**

#### TENDER PHASE:

13. Schools Redevelopment Consultant Eslyn Henley Richiez
14. Recreational Facilities Consultant
15. Project Management (PMSC)
16. Procurement Specialist
17. Ferry Terminal (West End)
18. ICT Schools, Offices, Courts

**UPDATED TOTAL: \$2,180,000 USD**

### GOODS

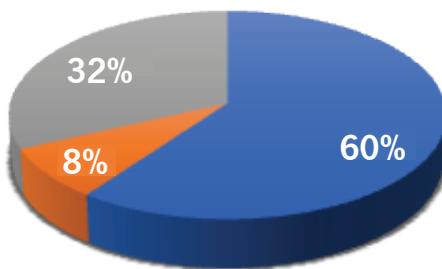

■ Signed  
■ Contract Awarded  
■ Tender phase

**TOTAL BUDGET OF 25 GOODS  
\$4,569,000 USD**

- 15 of 25 Contracts for goods have been signed
- 2 goods have been awarded contracts (to be signed)
- 8 goods are in tender phase

#### CONTRACTS SIGNED:

1. Seismic Stations
  2. Weather Stations
  3. Radio Data System
  4. Emergency Broadcast Encoder
  5. FM Fixed Transmitter & FM Mobile Transmitter
  6. DDM Vehicles
  7. School Books
- FEB. UPDATE
8. Marine Radios
  9. VSAT
  10. Land Mobile Radio Repeaters
  11. Marine Repeaters
  12. Land Mobile Radio Handhelds
  13. VHF Base Stations
  14. 2 M Handheld Radios
  15. High Frequency Base Stations

**UPDATED TOTAL: \$575,208 USD**

#### CONTRACTS AWARDED (to be signed):

16. Emergency Management Weather Information Network
- FEB. UPDATE
17. Seismic and Weather Monitoring Equipment- Tidal Gauge

**UPDATED TOTAL: \$105,400 USD**

#### TENDER PHASE:

18. School Supplies Primary and Secondary
19. Emergency Telecom and Early Warning alert network - Sirens
20. Restoration of Cane Garden Bay Pump Stations - Procurement Pumps and generators:
21. Emergency Telecom and Early Warning alert network - CATV Encoder and Character Generator
22. Emergency Telecom and Early Warning alert network - AM Transmitter
23. ICT for Schools
24. Police ICT Equipment
25. LAN/WAN equipment

**UPDATED TOTAL: \$2,311,000 USD**

**To join our next community meetings and get updates on the RRL follow us on:**



#### For more information:

Ministry of Finance Projects Unit  
2<sup>nd</sup> Floor, Qwomar Trading Building #2  
Road Town, Tortola VG1110  
Tel: 1(284) 494 3701- ext. 2144  
[www.bvi.gov.vg/rrl](http://www.bvi.gov.vg/rrl)

### OTHER RRL NEWS

#### WORKS

##### DDM/NEOC BUILDING

The tender document for the rehabilitation of the DDM Building will be launched shortly. Contractors look out for the opportunity for the DDM Building works.

##### ELMORE STOUTT HIGH SCHOOL

The bid opening for the L-shaped building of the school took place 30 January and the tender process is in the final stage. The objective is to start the works as soon as possible so that the building can be ready for the upcoming school year.

#### COMMUNITY MEETINGS

The first set of meetings were successfully held in Road Town, East End and Cane Garden Bay and allowed community members to obtain more information on the RRL and share questions and concerns with regards to the implementation of the different projects. Meetings will now continue in Anegada, Virgin Gorda and Jost Van Dyke.
